Activity ID	Activity Description	Orig Dur	Rem Dur	%	Early Start	Early Finish
1000	Develop Qualification RFP	10	0	100	20JUN11A	01JUL11A
1010	Proposers Submit Qualifications - RFP Response	15	0	100	01JUL11A	22JUL11A
1015	Develop Detailed Proposal RFP	30	0	100	08JUL11A	22AUG11A
1020	Evaluate Proposer Qualifications - Short List	21	0	100	25JUL11A	22AUG11A
1022	Community Meeting ASAC - Review Detailed RFP	1	0	100	02AUG11A	02AUG11A
1024	FCCPS - Review Proposer Qualifications Mtg	1	0	100	08AUG11A	08AUG11A
1026	FCCPS - Review Proposer Qual - Short List - Mtg	1	0	100	18AUG11A	18AUG11A
1040	School Board Approve Short List and RFP	1	0	100	23AUG11A	23AUG11A
1050	Proposers Submit Detailed RFP Proposals	20	0	100	24AUG11A	04OCT11A
1060	Evaluate Detailed Proposal - Recommend Firm	24	0	100	05OCT11A	07NOV11A
1065	Proposer Interview Presentations	1	0	100	12OCT11A	12OCT11A
1080	School Board Approve Firm for Negotiations	1	0	100	08NOV11A	08NOV11A
1090	Negotiate Comprehensive Agreement	24	0	100	09NOV11A	12DEC11A
1110	School Board Approve Comprehensive Agreement	1	0	100	13DEC11A	16DEC11A
2000	Design Thomas Jefferson - City Permit Rev & App	120	116	3	19DEC11A	29MAY12
2010	Thomas Jefferson Elementary Construction	240	240	0	30MAY12	30APR13
2020	Construction Contingency	40	40	0	01MAY13	25JUN13
3000	Project Complete	0	0	0		25JUN13

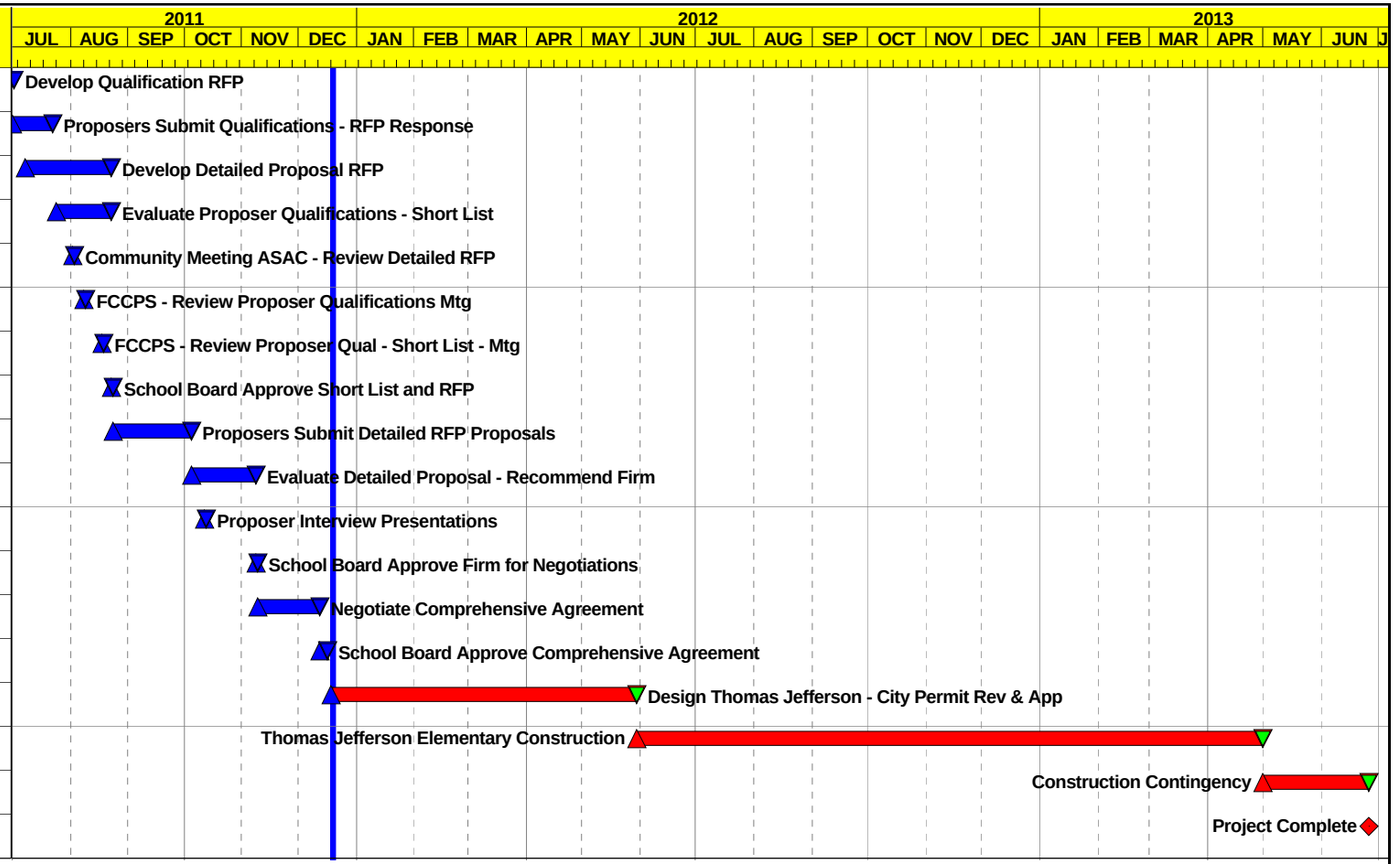

Start Date 01JUL11
Finish Date 25JUN13
Data Date 20DEC11
Run Date 19DEC11 09:43

Early Bar
Float Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

TJES

Sheet 1 of 1

Falls Church City Public Schools

Thomas Jefferson Elementary School

MASTER SCHEDULE

Date	Revision	Checked	Approved
